KCCD Facilities Planning & Construction Report 2012 – 13

(unaudited)

4th Quarter Ending June 30, 2013

Overview

District SRID Spending (MG100) by:

- Summary
- By College
- By Site


District Program Overview

- Construction
- Design
- Planning/ Administrative & Research


District SRID Spending thru 2012-13 4th Quarter June 2013 Summary


Original Measure G Budget: \$180,000,000
Interest & Other Revenues: \$22,113,494
Total Funds available: \$202,113,495
Total Funds spent to date: \$111,435,327
Total Funds available for use: \$90,678,167

District SRID Spending through 2012-13 4th Qtr June 2013

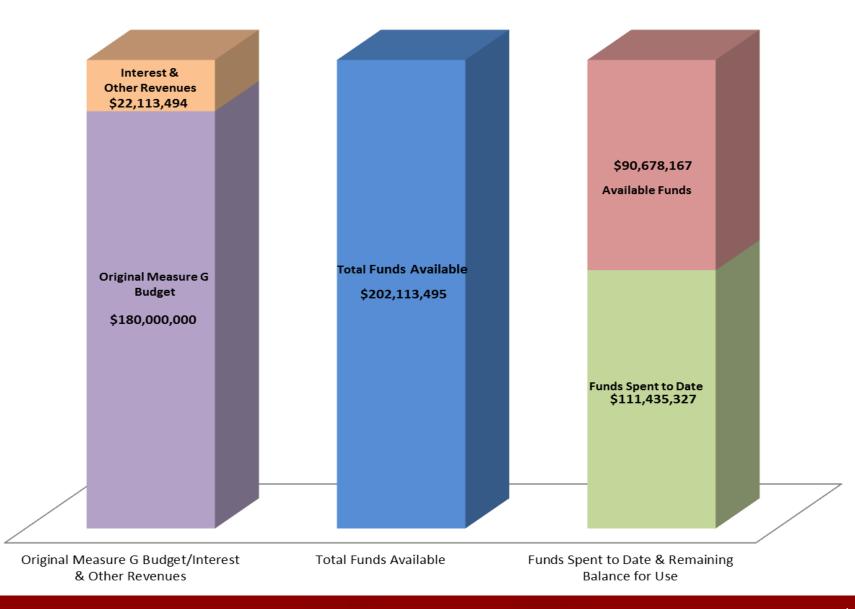

District SRID Spending thru 2012-13 4th Qtr June 2013

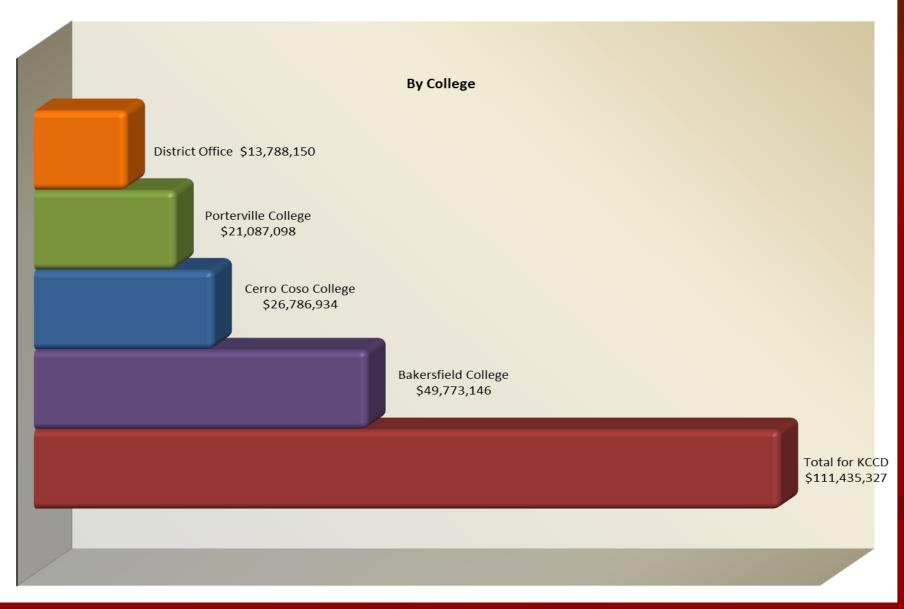

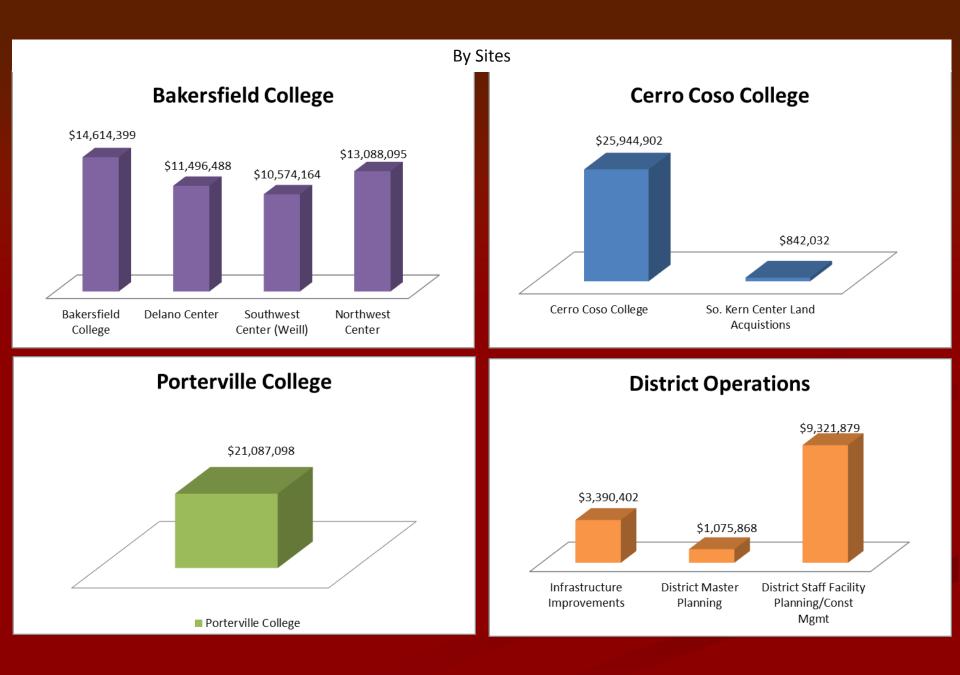

District Program Overview Construction 4th Qtr. June 2013

No.	Currently in Construction Phase	Budget					Construc	tion	Comments
			Budget Spent to date Source		% Construction Complete	Change Order %	Description		
	Bakerfield College								
1	Admin Building Entry Door Replacement	\$	29,715	\$	19,945	SRID	99%	0.00%	Closeout in process
2	Baseball Clubhouse Phone/Fiber Conduit	\$	61,737	\$	45,000	SRID	99%	0.00%	Closeout in process
3	Bookstore Barnes & Noble	\$	260,000		-0-	B & N	90%	0.00%	Lease Agreement
4	Business Ed Summer Projects	\$	165,000	\$	60,965	SRID/Campus	50%	0.00%	
5	Campus Water & Gas Line (Phase 1 & 2)	\$	3,920,200	\$	218,944	SRID	10%	0.00%	
6	Central Chiller Plant Replacement	\$	2,063,830	\$	262,052	SRID	7%	0.00%	Equipment Purchased
8	FACE Bldg Summer Project	\$	82,000	\$	40,196	SRID/Campus	90%	0.00%	
9	Fine Arts Summer Project	\$	201,000	\$	13,144	SRID/Campus	7%	0.00%	
10	GET Facility	\$	1,229,912	\$	22,213	GET/Campus	99%	N/A	Primarily GET Funded
11	Language Arts Building Entry Door Replacement	\$	57,925		-0-	SRID	0%	0.00%	
12	Math & Science Roof Repairs	\$	18,993	\$	16,863	SRID/Campus	99%	0.00%	Closeout in process
13	Performing Arts Modernization (SAM)	\$	15,895,640	\$	2,616,532	SRID/State	7%	0.00%	
14	Photo Voltaic	\$	9,292,500	\$	8,494,088	CEG/ Lease Rev Bonds/Campus	99%	2.49%	Closeout in process
15	Science & Engineering Roof Repairs	\$	593,800	\$	268,326	SRID/Campus	30%	0.00%	
16	Science Engineering Summer Project	\$	175,000	\$	93,724	SRID/Campus	45%	0.00%	
17	Student Services Building Entry Door Replacement	\$	88,637		-0-	SRID	0%	0.00%	
18	Thermal Energy System Phase 2	\$	688,224	\$	596,885	Campus	99%	0.64%	Commissioning in process
	Weill Center								
19	NORAD HVAC Upgrades	\$	356,800		\$343,717	SRID	99%	6.15%	Closeout in process
	Porterville College								
20	Fine Arts HVAC Replacement	\$	78,900		\$33,364	SRID/Campus	99%	0.00%	Closeout in process
21	Fire Lane/ ADA Parking Lots	\$	562,119		\$76,380	SRID/Campus	35%	0.00%	
22	Gym Water Heater Tank Replacement	\$	24,600	\$	500	SRID/Campus	60%	0.00%	Closeout in process
23	Math Science HVAC, Boilers, Water Heaters, Pumps	\$	974,548	\$	522,790	SRID/Campus	22%	0.00%	
	Student Center ReRoof	\$	855,359	\$	549,275	SRID/Campus	8%	0.00%	
25	Main Campus Electrical Upgrade	\$	517,500	\$	46,227	SRID	99%	0.00%	Scope Reduction

District Program Overview Design 4th Qtr. June 2013

No.	Currently in Design Phase	Budget					De	esign	Comments
			Budget	Spe	ent to date	Project Funding Source	% Design complete	Revised Work Authorization %	Description
	Bakersfield College								
1	Performing Arts East Side Improvements	\$	1,303,872	\$	41,612	SRID	50%	0%	
2	NE Parking Lot ADA & Shade Structure	\$	365,453	\$	3,259	SRID	95%	0%	DSA Reviewing
3	Elevators Repair and Replace	\$	353,873	\$	106,393	SRID	55%	5%	
4	Language Arts Basement Fireproofing	\$	62,000		-0-	SRID/Campus	0%	0%	
	Delano Center			-					
5	Fire Alarm Certification for DSA	\$	26,044	\$	6,235	Campus	80%	0%	
	Weill Center								
6	Parking Lot Upgrades	\$	190,900	\$	24,889	Other	95%	0%	DSA Reviewing
7	KCCD Security Planning - Weill Only	\$	25,846	\$	25,846	SRID	100%	0%	
	Cerro Coso College								
8	Main Building Modernization	\$	15,354,088	\$	223,926	SRID	15%	0%	Design Development
9	Campus Wide Fire Alarm Integration	\$	131,055	\$	14,915	SRID	53%	0%	
10	Gym HVAC Replacement	\$	840,900	\$	68,353	SRID/Campus	75%	4.7%	
11	Occupational Lab Reroof/HVAC/Welding Exp	\$	1,287,041	\$	86,899	SRID/Campus	95%	0%	DSA Reviewing
12	Occupancy & Evacuation Signage	\$	84,020	\$	27,203	Campus	90%	0%	
	Mammoth								
13	Monument Sign	\$	87,765		-0-	Other	60%	0%	
	Porterville College								
14	Gymnasium Reroof & HVAC Replacement	\$	2,818,325	\$	62,234	SRID/Campus	20%	0%	
15	Path of Travel - to Main Street	\$	126,400	\$	14,811	SRID	73%	0%	
16	Central Plant and Chiller Loop	\$	1,300,000	\$	24,080	SRID	40%	0%	
17	Asphalt Plano Fire Lanes (Plano to Main)	\$	363,400		-0-	SRID/Campus	0%	0%	
								· · · · · · · · · · · · · · · · · · ·	
No.	Currently in Planning & Studies Phase	Budget					Design		Comments
		Forecast Cost Spent to date Funding Source				Funding Source	% Co	omplete	
1	Transition plans	\$	130,000	· · · · · · · · · · · · · · · · · · ·		100%			
2	Construction Standards	\$	110,000	\$ 88,514		80%		In Final Internal Review	
3	CEQA	\$	100,000		-0-			0%	

District Program Overview Planning 4th Qtr. June 2013

No.	Planned Capital Outlay / State & Local Funding		Comments		
	Final Project Proposals (FPPs)	State \$	Local \$	Total	FPP Approved
1	BC Student Services Modernization	\$ 19,052,000	\$ 3,333,000	\$22,385,000	Yes
2	DC LRC Multi Purpose Building	\$ 28,385,000	\$ 4,576,000	\$32,961,000	Yes
3	PC Allied Health Facility	\$ 10,925,000	\$ 5,067,000	\$15,992,000	Yes
4	BC Language Arts Remodel for Efficiency	\$ 7,921,000	\$ 4,414,000	\$12,335,000	Pending/ Dec '13
	Initial Project Proposals (IPPs)				IPP Submitted

	Initial Project Proposals (IPPs)				IPP Submitted
5	BC Fine Arts Remodel for Efficiency	\$ 12,127,000	\$ 2,800,000	\$14,927,000	Yes
6	BC Science & Engineering Replacement	\$ 30,242,000	\$ 14,500,000	\$44,742,000	Yes
7	PC Career Technology Building	\$ 7,983,120	\$ 7,983,120	\$15,966,240	Yes
8	PC Human Performance and Kinsiology	\$ 5,059,000	\$ 5,058,000	\$10,117,000	Yes

District Administrative & Research 4th Qtr. June 2013

No.	Administrative & Research Activities	Description					
1	Accounting and Reporting (CM14 and P6)	Integration of systems					
2	Design Guidelines						
3	Document Management	Blueprints/ Project Files					
4	DSA Buildings Certification						
5	Energy saving, Energy management, Energy generation	Working with CCC/IOU for Prop 39 Projects					
6	Fire Alarm Systems						
7	Five-year Facilities Plan						
8	Informational Website Development	Assisting IT Department					
9	Security & Mass Notification	Assisting IT Department					
10	Utilities Mapping						

MEASURE G OVERSIGHT COMMITTEE ACTIVITIES Conclusion:

The Oversight Committee finds the District to be in compliance with the requirements of Article XIIA, Section 1(b)(3) of the California Constitution.

