

# Facilities Planning & Construction Report 2015 - 16

2<sup>nd</sup> Quarter Ending December 31, 2015









## **Overview**

- District SRID Spending (MG100)
  - Summary
  - By College
  - By Site
- District Program Overview
  - Construction
  - Design
  - Planning/ Administrative & Research
- Selected Photographs




# District SRID Spending Summary

- Original Measure G Budget: \$ 180,000,000
- Interest & Other Revenues: \$ 23,043,193
- Total SRID Funds: \$203,043,194
- Total Funds Spent To Date: \$139,235,821
- Total Funds Unspent To Date: \$ 63,807,373




#### **SRID Overall Expenditures**

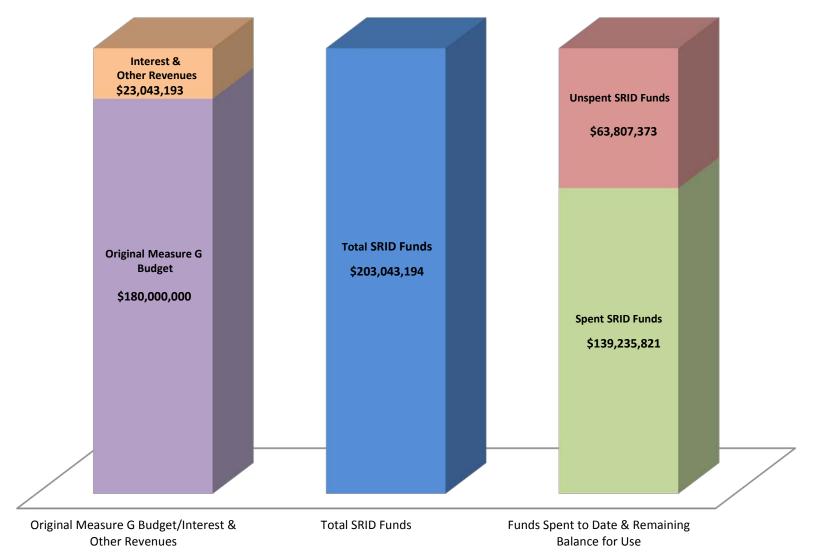





#### **SRID Expenditures By College**

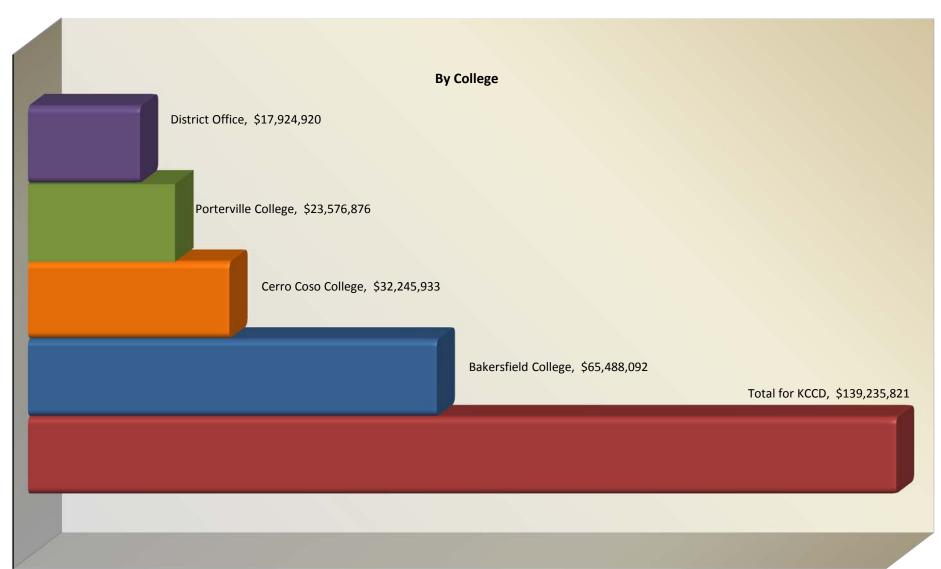





#### **SRID Expenditures By Site**

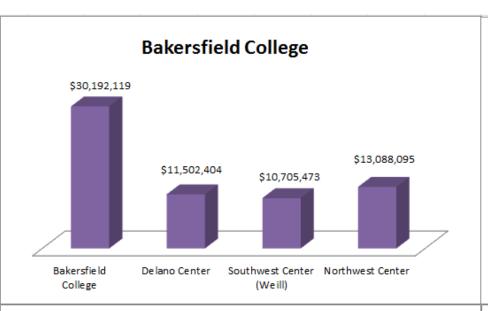

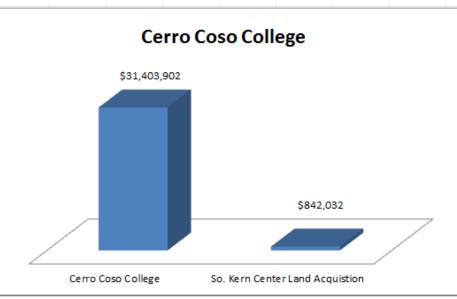


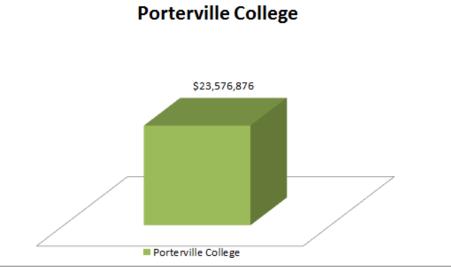

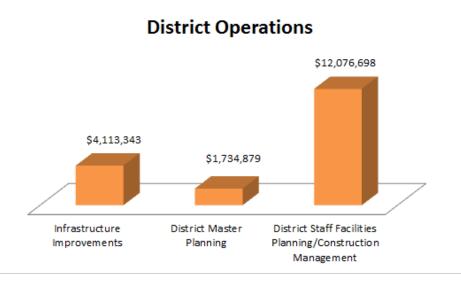



## **Unspent SRID Funds By College**

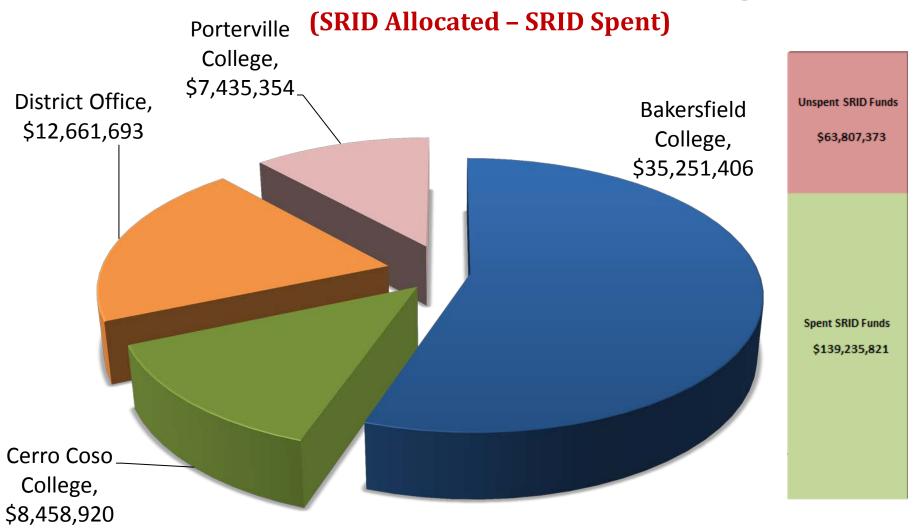



# District Program Overview Completed Projects 2<sup>nd</sup> Quarter Ending December 31, 2015

4														
Campus	Туре	Project Name	Project Organization Code	Project Status	Current Total Project Budget	Total Project Expenditures		Completion Date	Anticipated DSA Close Date	I Project Flinding	Construction /Design % Complete	Project % Complete	_	Comments
ВС	CAP	SWC Modernization DSA Closeout	FA3009	1 - Complete	\$ 136,204	\$ 91,424	Dec-15	Mar-14	Apr-15	SRID	100%	100%	0.0%	DSA Certified
ВС	CAP	BC Performing Arts East Side Improvements	FA1054	1 - Complete	\$ 1,699,713	\$ 1,504,566	Nov-14	May-15	Oct-15	SRID	100%	100%	2.7%	DSA Certified
ВС	SM	BC NE Parking Shade Structure	FA1103	1 - Complete	\$ 365,453	\$ 325,104	Mar-14	Jun-14	Mar-15	SRID	100%	100%	2.0%	DSA Certified
ВС	SM	BC Central Chiller Plant Replacement	FA1102	1 - Complete	\$ 2,711,528	\$ 2,707,827	Nov-13	Dec-14	Mar-15	SRID	100%	100%	2.7%	DSA Certified
ВС	SM	BC Campus Wide Water and Gas Line Replacen	r FA1101	1 - Complete	\$ 3,920,200	\$ 3,696,212	Mar-14	Mar-15	Jun-15	SRID	100%	100%	22.5%	DSA Certified
ВС	SM	Weill Overflow Parking Lot and Remediation	FA3001	1 - Complete	\$ 167,644	\$ 104,443	May-15	Feb-15	Jun-15	Campus	100%	100%	0.0%	
ВС	SM	Weill Inst Main Parking Lot Replacement	FA3015	1 - Complete	\$ 190,900	\$ 912,078	May-15	Aug-14	Nov-14	Campus	100%	100%	0.0%	
ВС	SM	Weill HVAC Replacement	FA3016	1 - Complete	\$ 275,000	\$ 275,000	May-15	Aug-15	Dec-15	State	100%	100%	0.0%	
ВС	SM	BC Chairs/Elevator Repairs & Replacement	28F144	1 - Complete	\$ 798,000	\$ 782,418	Feb-15	Sep-14	Nov-15	SRID	100%	100%	3.0%	DSA Certified
PC	SM	PC Campus Security Upgrades Phase 1	FC1024	1 - Complete	\$ 32,100	\$ 26,888	Aug-14	Oct-15	N/A	SRID	100%	100%	0.0%	
PC	SM	PC Central Plant & Chiller Loop	FC1079	1 - Complete	\$ 1,300,000	\$ 796,498	Feb-14	Oct-14	Feb-15	SRID	100%	100%	13.9%	DSA Certified
PC	SM	PC Sci Math HVAC/Boiler/H2O Htr Replacemen	58F106/PCM010	1 - Complete	\$ 974,548	\$ 968,268	Aug-14	Jan-15	Dec-14	SRID/Campus	100%	100%	4.5%	DSA Certified
PC	SM	PC Student Center Roof Repairs	58F110	1 - Complete	\$ 1,268,264	\$ 1,178,384	Apr-15	Jan-15	Oct-15	SRID/Campus	100%	100%	48.5%	DSA Closeout Pending
PC	SM	PC On Campus Path of Travel	FC1064	1 - Complete	\$ 159,696	\$ 119,738	Feb-14	Jun-15	Oct-15	SRID	100%	100%	0.0%	DSA Closeout Pending
PC	SM	PC Prop 39 Lighting Replacement Year Two	FC1081	1-Complete	\$ 92,734	\$ 83,359	Jun-15	Sep-15	N/A	Prop 39	100%	100%	0.0%	
BC	CAP	BC GET Facility	28F758	1- Complete	\$ -	\$ 32,580	Apr-11	Dec-13	Jun-15	GET/Campus	100%	100%	0.0%	DSA Certified



# District Program Overview Construction Projects 2<sup>nd</sup> Quarter Ending December 31, 2015

4														
Campus	Туре	Project Name	Project Organization Code	Project Status	Project	Total Project Expenditures		Completion Date	Anticipated DSA Close Date	Project Funding Source	I /Design %	Project % Complete	_	Comments
ВС	CAP	BC Performing Arts Modernization	28F740	2 - Construction	\$ 19,273,903	\$ 16,542,286	Jun-13	Sep-15	Dec-15	SRID/State	100%	100%	2.7%	
BC	CAP	BC STEM Building	FA1094	2 - Construction	\$ 500,000	\$ 82,900	Oct-15	May-16	Aug-16	SRID/Campus	100%	10%	0.0%	
BC	SM	BC STEM Room 26 and 27 Renovation	FA1047	2 - Construction	\$ 182,464	\$ 828	May-14	Feb-15	Jul-15	RP207	100%	95%	0.0%	Design for DSA Close-out
ВС	SM	DC Fire Alarm Cert DSA	FA2012	2 - Construction	\$ 32,894	\$ 31,877	Jun-14	Nov-14	Jun-16	SRID	99%	99%	27.6%	Pending DSA Closeout documents
ВС	SM	BC Student Services Air Handlers and Chiller Re	FA1033	2 - Construction	\$ 1,171,163	\$ 958,468	Mar-15	Nov-15	Mar-16	SRID	100%	20%	0.0%	
ВС	SM	BC Football Practice Field Lighting	FA1038	2 - Construction	\$ 290,700	\$ 23,880	Dec-15	Feb-16	May-16	SRID	95%	35%	0.0%	
ВС	SM	BC Prop 39 Lighting Replacement Year 2	FA1039	2 - Construction	\$ 377,503	\$ 301,265	Jun-15	Aug-15	Nov-15	Prop 39	100%	99%	0.0%	Pending PG&E Close-out
BC	SM	BC Gymnasium Air Conditioning	FA1112	2 - Construction	\$ 661,232	\$ 45,950	Nov-15	Aug-16	Dec-16	SRID	5%	0%	0.0%	
ВС	SM	BC Path of Travel	FA1115	2 - Construction	\$ 438,564	\$ 31,369	May-16	Oct-16	Dec-16	SRID/State	100%	30%	0.0%	
CC	CAP	CC Main Building Modernization	FB1062	2 - Construction	\$ 16,900,000	\$ 4,105,507	Aug-15	Dec-16	Mar-17	SRID	100%	25%	0.6%	
CC	SM	CC Occ Lab Reroof/HVAC/Welding Expan	FB1004	2 - Construction	\$ 1,287,041	\$ 1,087,807	Feb-14	Jan-15	Sep-15	SRID/Campus	99%	99%	1.6%	Pending DSA Certification
DO	CAP	DO Facilities IT Improvements	18F104	2 - Construction	\$ 213,003	\$ 197,163	Jul-11	Ongoing	N/A	SRID	93%	93%	0.0%	
DO	CAP	DO District-wide Wireless Networking	FA3013	2 - Construction	\$ 57,275	\$ 106,945	Apr-12	Ongoing	N/A	SRID	90%	90%	0.0%	
DO	CAP	DO Telephone System Replacement 2014	FD1006	2 - Construction	\$ 350,000	\$ 336,269	Jun-13	Ongoing	N/A	SRID	96%	96%	0.0%	
DO	CAP	Network Systems	FD1020	2 - Construction	\$ 575,000	\$ 319,082	Jun-12	Ongoing	N/A	SRID	55%	55%	0.0%	
DO	SM	Weill Inst. Prop 39 Lighting Year Two	FD1024	2 - Construction	\$ 80,830	\$ 60,982	Jun-15	Aug-15	Dec-15	Prop 39	100%	99%	0.0%	Pending PG&E Close-out
DO	SM	Weill HVAC Replacement Phase 2	FA3018	2 - Construction	\$ 250,000	\$ 5,268	May-16	Jun-16	N/A	State	75%	25%	0.0%	
PC	CAP	PC Photovoltaic System	FC1073	2 - Construction	\$ 4,600,000	\$ 3,586,462	Sep-15	Feb-16	May-16	Loan	100%	99%	0.0%	Punch items
PC	SM	PC Asphalt Plano Fire Lane	FC1030	2 - Construction	\$ 477,013	\$ 429,648	May-15	Sep-15	Apr-16	SRID/Campus	100%	100%	0.6%	
PC	I SM	PC Allied Health HVAC.Reroof.Floor.Transform	FC1037	2 - Construction	\$ 308,212	\$ 326,127	May-15	Jan-16	N/A	State	100%	100%	0.0%	



## District Program Overview Design Projects 2<sup>nd</sup> Quarter Ending December 31, 2015

Campus	Туре	Project Name	Project Organization Code	Project Status	Current Total Project Budget	Total Project Expenditures		Completion Date	Anticipated DSA Close Date	Project Filinding	/Design %	Project % Complete		Comments
ВС	CAP	BC Maintenance and Operations Building	FA1078	3 - Design/Bid	\$ 4,774,149	\$ 245,766	Dec-15	TBD	TBD	SRID	100%	25%	0.0%	Design pending DSA Approval
ВС	SM	BC Language Arts Basement Swing Space	FA1100	3 - Design/Bid	\$ 5,509,000	\$ 116,658	Aug-17	May-17	Aug-18	SRID/Campus	0%	0%	0.0%	Scope & Budget, Site Relocation to Mt. Vernon
ВС	SM	BC Fire Alarm Repair and Code Compliance	FA1116	3 - Design/Bid	\$ 1,118,310	\$ 134,741	Oct-15	Oct-15	Jan-16	State	25%	2%	0.0%	Design
ВС	SM	BC Exterior Wayfinding	FA1117	3 - Design/Bid	\$ 431,700	\$ 18,900	May-16	Sep-16	N/A	SRID/Campus	100%	25%	0.5%	
CC	SM	CC Prop 39 Yr 3 Ext Lighting	FB1064	3 - Design/Bid	\$ 167,386	\$ 6,800	Feb-16	Apr-16	N/A	Prop 39/Campus	98%	25%	0.0%	
CC	SM	Mammoth Science Expansion	FB5023	3 - Design/Bid	\$ 461,700	\$ 1,920	Dec-16	Aug-17	Oct-17	Mammoth	5%	2%	0.0%	
DO	CAP	District Wide Security Access Hardware	FD1025	3 - Design/Bid	\$ 4,700,000	\$ 158,686	Apr-15	Apr-17	N/A	SRID	100%	30%	0%	Awaiting Bid Award
DO	CAP	DO Surveillance Cameras	FA3017	3 - Design/Bid	\$ 42,000	\$ 39,885	Aug-15	Oct-15	N/A	SRID	100%	100%	0.0%	
DO	CAP	DO Public Address Notification	FD1026	3 - Design/Bid		\$ 17,900			TBD					
PC	SM	PC Gymnasium Roofing	FC1005	3 - Design/Bid	\$ 2,900,000	\$ 214,830	Apr-16	Dec-16	Apr-17	SRID/Campus	100%	0%	0.0%	Bidding
PC	SM	PC Prop 39 Year 3 Exterior Lighting	FC1082	3 - Design/Bid	\$ 98,297	\$ 4,800	Apr-16	Jun-16	N/A	Prop 39	90%	3%	0.0%	Design



### **District FPP and IPP Planning Activities**

Project	Total Budget	State Contribution	<b>Local Contribution</b>	Туре
BC Language Arts Remodel for Efficiency	\$15,321,000	\$9,983,000	\$5,338,000	FPP
PC Allied Health Facility	\$16,719,000	\$11,482,000	\$5,237,000	FPP
FPP Total	\$32,040,000	\$21,465,000	\$10,575,000	
BC Fine Arts Remodel for Efficiency	\$15,546,000	\$12,746,000	\$2,800,000	IPP
BC Science and Engineering Replacemen	\$47,350,000	\$27,930,000	\$19,420,000	IPP
BC Student Services Modernization	\$15,686,000	\$12,839,000	\$2,847,000	IPP
BC Welcome Center	\$4,789,000	\$4,073,000	\$716,000	IPP
DC LRC	\$25,992,000	\$23,133,000	\$2,859,000	IPP
PC Career Technology Building	\$15,966,000	\$7,983,000	\$7,983,000	IPP
PC Human Performance and Kinesiology	\$11,860,000	\$5,930,000	\$5,930,000	IPP
PC Student Services Modernization	\$8,848,000	\$4,273,000	\$4,273,000	IPP
IPP Total	\$146,037,000	\$99,209,000	\$46,828,000	




## BC Maintenance & Operations





## **BC Chairlift & Elevator Repairs**

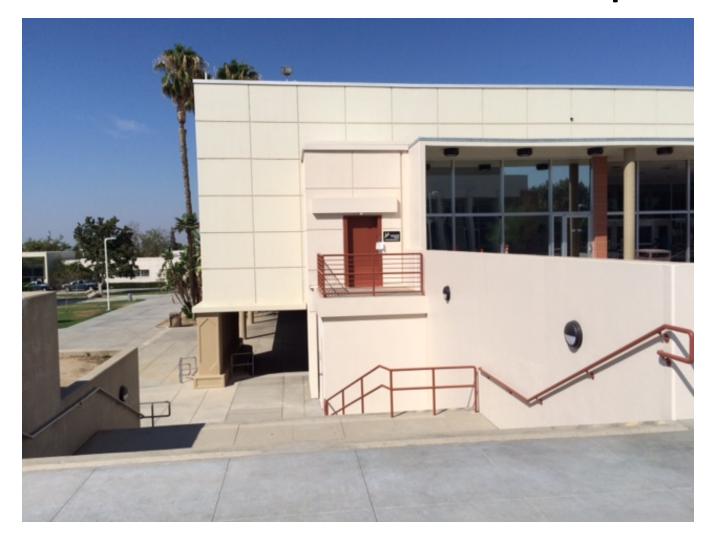



### **BC STEM Building**



Southeast View

# Bakersfield College Kern Community College District BC STEM Grant Building Project



## CC Main Building Modernization





## PC Allied Health HVAC Replacement



#### BOND OVERSIGHT COMMITTEE LISTING

#### **Committee Chair- Vacant**

Vice Chair- Vacant

Bruce Massa (October 2015-September 2017)

Jennifer M. Wood-Slayton (September 2014-August 2016)

Matthew Anderson (December 2014-November 2016)

Michael O'Doherty (March 2016-February 2018)

Milt Stowe (March 2016-February 2018)

Jesse Frederick (March 2016-February 2018)

#### **Student Trustee:**

Lily Nelson (October 2015-September 2017)



# Questions?
