

Facilities Planning & Construction Report 2018 - 19

1st Quarter Ending September 30, 2018









Overview

- District SRID Spending (MG100)
 - Summary
 - By College
 - By Site
- District Measure J Spending (MJ100)
 - Summary
 - By College
 - By Site
- District Program Overview
 - Construction
 - Design
 - State Funding Opportunities
 - Selected Photographs



District SRID Measure G Spending Summary

• Original Measure G: \$ 180,000,000

Interest & Other Revenues: \$ 24,936,987


• Total SRID Funds: \$204,936,987

Total Funds Spent To Date: \$170,436,579

Total Funds Unspent To Date: \$ 34,500,408




SRID Overall Expenditures

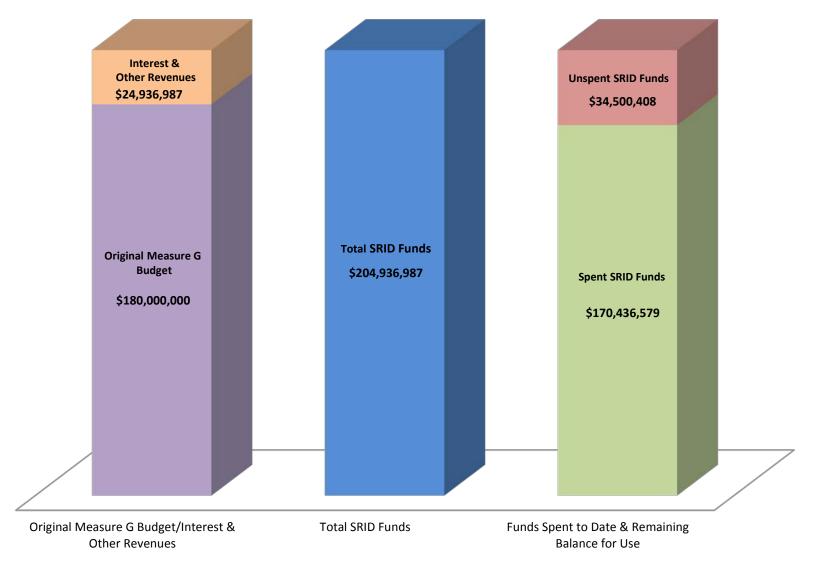




SRID Expenditures By College

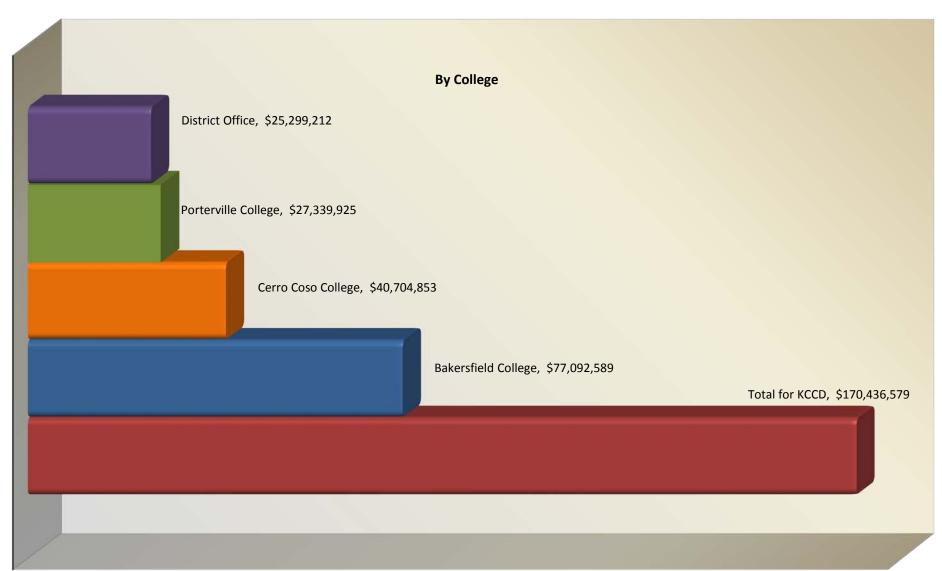




Unspent SRID Funds By College

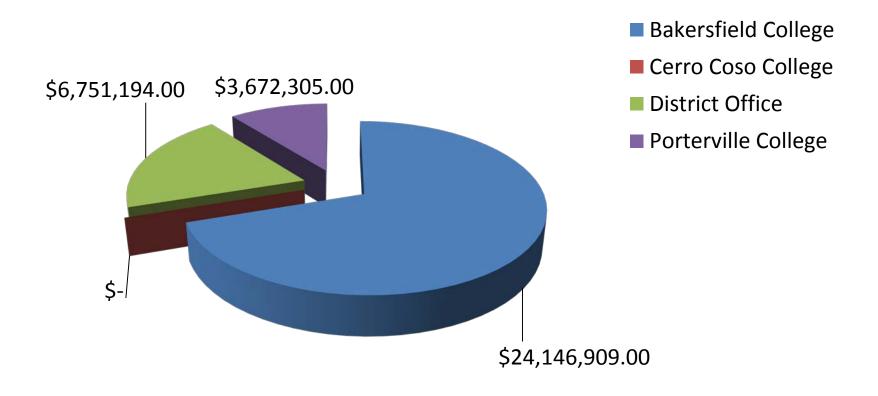


District Measure J Spending Summary

- Original Measure J Budget: \$502,821,000
- Interest & Other Revenues: \$622,477
- Total Measure J Funds: \$503,443,477
- Total Funds Spent To Date: \$16,310,963
- Total Funds Unspent To Date: \$ 487,132,514


Measure J Overall Expenditures

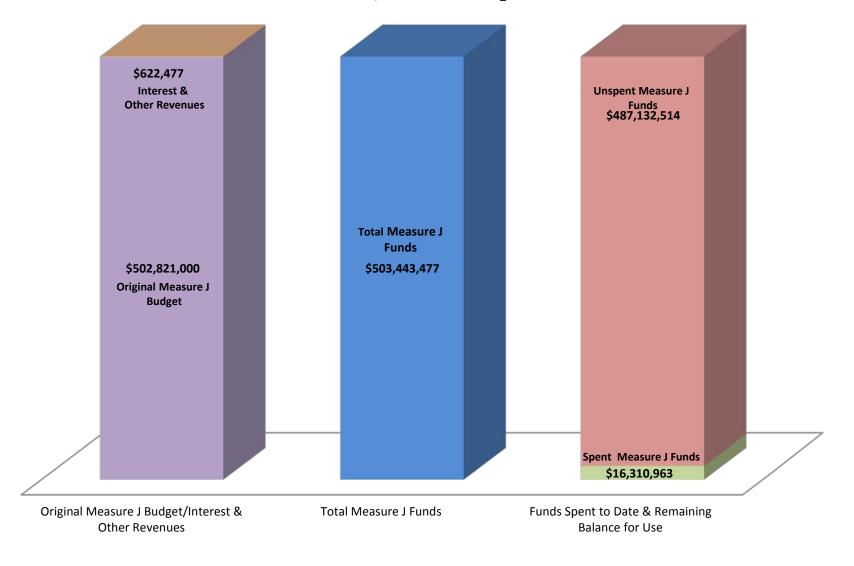

Measure J Allocations by College

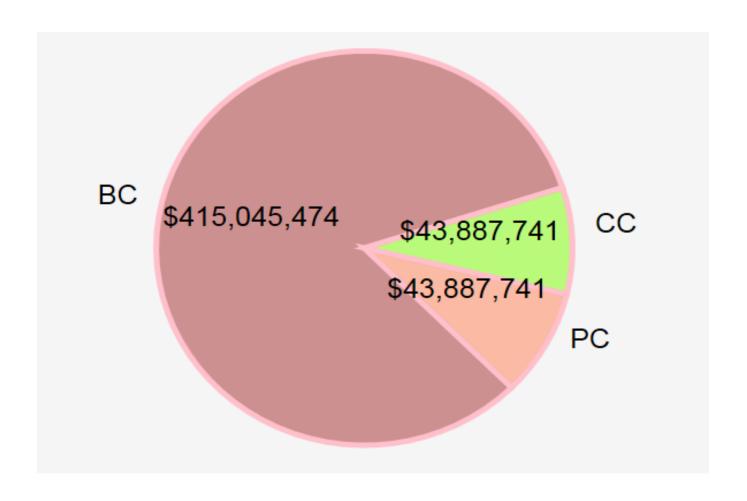


Measure J Expenditures By College

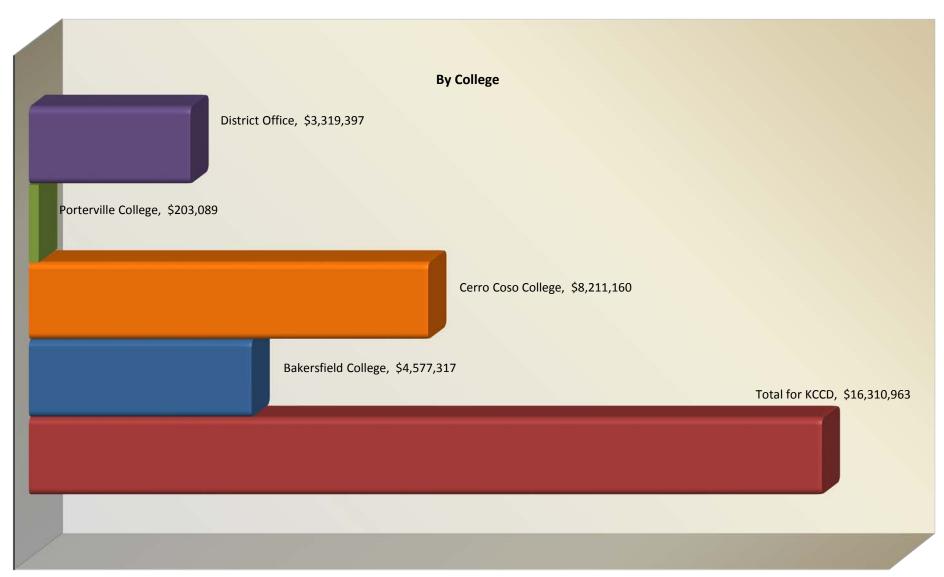

Unspent Measure J Funds By College

Funds Remaining to Spend by Campus

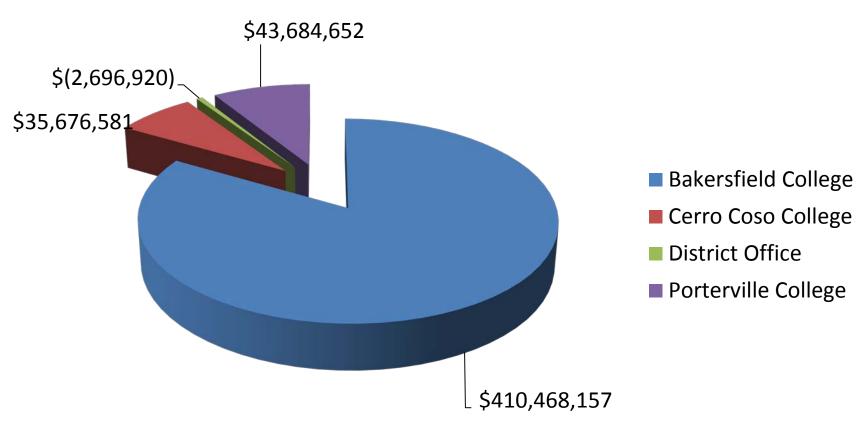



District Program Overview Completed Projects 1st Quarter Ending September 30, 2018

Campus	Туре	Project Name	Project Organization Code	Project Status	otal Project openditures	Start Date	Completion Date	Anticipated DSA Close Date	Project Funding Source	Construction /Design % Complete	Project % Complete	
ВС	SM	BC Swing Space	FA1100	1 - Complete	\$ 508,716	Aug-17	Jul-18	Aug-18	SRID/Campus	100%	100%	0.0%
ВС	CAP	BC Maintenance and Operations Building	FA1078	1 - Complete	\$ 5,803,722	Dec-15	May-18	May-18	SRID	100%	100%	0.0%
ВС	SM	BC Window Covering Replacement	FA1124	1 - Complete	\$ 44,941	Nov-16	Dec-17	N/A	State	100%	100%	0.0%
ВС	SM	Gym Storefront Door Systems Replacement SMSR 14-	28F775	1 - Complete	\$ -	May-18	Jan-18	N/A	State	0%	0%	0.0%
ВС	SM	BC SMSR Interior Painting, Multiple Buildings	FA1122	1 - Complete	\$ 154,990	Nov-16	Feb-18	N/A	State	100%	100%	0.0%
ВС	SM	BC Pool Lighting Replacement SMSR 2014-15	28F776	1 - Complete	\$ 30,000	Feb-18	May-18	N/A	State	100%	100%	0.0%
ВС	SM	BC Campus Wide Window Covering Replmt Phase III:	28F772	1 - Complete	\$ -	May-18	May-18	N/A	State	100%	100%	0.0%
ВС	SM	BC SMSR Campus Wide ADA Entry Door Replacement	FA1126	1 - Complete	\$ 115,000	Nov-17	Aug-18	N/A	State	100%	100%	0.0%
ВС	SM	BC Roofing Repairs	FA1118	1 - Complete	\$ 1,105,468	May-16	Apr-18	N/A	State	100%	100%	0.0%
ВС	SM	BC Prop 39 Year 4 Exterior Lighting	FA1120	1 - Complete	\$ 542,040	Oct-16	May-18	N/A	Prop 39	100%	100%	0.0%
CC	SM	CC Prop 39 Yr 4 Exterior Lighting	FB1066	1 - Complete	\$ 122,293	Feb-17	Jan-18	N/A	Prop 39/Campus	100%	100%	0.0%
PC	SM	PC SMRS Roofing Repairs & Replacement	FC1087	1 - Complete	\$ 175,467	Jun-17	Feb-18	N/A	State/SRID	100%	100%	0.0%
PC	SM	PC Prop 39 Year 4 Exterior Lighting	FC1084	1 - Complete	\$ 129,700	Feb-17	Mar-18	N/A	Prop 39	100%	100%	0.0%
PC	SM	PC Campus Building & Wayfinding Signage	FC1088	1 - Complete	\$ 286,101	Apr-17	Jul-18	N/A	Campus	100%	100%	0.0%
PC	SM	PC SMSR Fire Lane/Service Road	FC1085	1 - Complete	\$ 79,031	Sep-16	Jul-18	N/A	State/Campus	100%	100%	0.0%
PC	SM	PC Veterans Monument	58F742	1 - Complete	\$ 91,001	Sep-17	Jul-18	N/A	Campus	100%	100%	0.0%
PC	SM	PC 2017-18 SMSR Irrigation Controller Replacement	58F745	1 - Complete	\$ 10,043	Apr-18	Aug-18	N/A	State/Campus	100%	100%	0.0%
ВС	SM	BC Child Care Fencing Replacement SMSR 14-15	28F778	1-Complete	\$ 30,000	Nov-17	Jan-18	N/A	State	100%	100%	0.0%
CC	SM	CC SMSR 2016-17 CDC Renovation	FB1065	1-Complete	\$ 155,437	Oct-16	Jul-18	N/A	State	100%	100%	0.0%
DO	SM	Weill SMSR 2016-17 EMS Replacement & Upgrade	FA3021	1-Complete	\$ 55,075	Oct-16	May-18	N/A	State	100%	100%	0.0%
DO	SM	Weill SMSR 2016-17 Fire Alarm Panel Replmt	FA3020	1-Complete	\$ 111,625	Oct-16	May-18	N/A	State	100%	100%	0.0%
PC	SM	PC Flooring Replacement, Various Building	58F738	1-Complete	\$ 276,690	May-17	Jul-18	N/A	SRID	100%	100%	0.0%



District Program Overview

Construction Projects 1st Quarter Ending September 30, 2018

Campus	Туре	Project Name	Project Organization Code	Project Status	otal Project penditures	Start Date	Completion Date	Anticipated DSA Close Date	Project Funding Source	Construction /Design % Complete	Project % Complete	_
BC	SM	DC Fire Alarm Cert DSA	FA2012	2 - Construction	\$ 48,778	Jun-14	Apr-17	Aug-17	SRID	100%	99%	27.6%
ВС	SM	BC HVAC Replacement	FA1125	2 - Construction	\$ 188,402	Dec-17	Jun-18	N/A	State	100%	100%	0.0%
BC	SM	BC Emergency Generator Repairs	FA1121	2 - Construction	\$ 42,196	Feb-18	Aug-18	N/A	State	100%	100%	0.0%
BC	SM	BC Interior and Exterior Building Painting SMSR 17-18	28F770	2 - Construction	\$ 159,448	Jun-18	Dec-18	N/A	State	100%	90%	0.0%
BC	SM	BC Fire Alarm Repair and Code Compliance	FA1116	2 - Construction	\$ 496,387	Jun-16	Dec-18	Dec-18	State	100%	90%	1.4%
BC	SM	BC EMS Replacement Phase 1	FA1123	2 - Construction	\$ 172,261	Nov-16	Dec-18	N/A	State	100%	90%	0.0%
BC	SM	BC HVAC/Boiler/Hot Water Heater Repl SMSR 17-18	28F769	2 - Construction	\$ 96,618	Jun-18	Dec-18	N/A	State	100%	80%	0.0%
BC	SM	BC Mulitiple Door Replacement SMSR 2014-15	28F781	2 - Construction	\$ 40,555	May-18	Dec-18	N/A	State	100%	100%	0.0%
BC	SM	Delano HVAC Lab	21AWL3	2 - Construction	\$ -	Aug-18	Dec-19	N/A	Campus	0%	0%	0.0%
BC	CAP	BC Parking Lot Rehabilitation (Infrastructure Phase 1)	28F761	2 - Construction	\$ 2,596,287	Feb-18	Oct-18	Dec-18	Measure J	100%	95%	0.0%
ВС	SM	BC Prop 39 Year 5 Interior Lighting	28F779	2 - Construction	\$ 603,311	Dec-17	Jul-18	N/A	Prop 39/Campus	100%	100%	0.0%
BC	SM	BC Campus Wide Ceiling Tile Replacement	28F773	2 - Construction	\$ 44,963	May-18	Dec-18	N/A	State	100%	100%	0.0%
ВС	SM	BC Campus Wide Flooring Replacement Phase II SMS	28F777	2 - Construction	\$ 339,435	Oct-17	Dec-18	N/A	State	100%	80%	
ВС	SM	DC Roofing Repairs (Main Building) SMSR 14-15	28F780	2 - Construction	\$ -	Mar-18	Dec-18	N/A	State	0%	0%	0.0%
ВС	SM	BC Window Covering Replacement Phase II (SMRS 17	28F771	2 - Construction	\$ 39,000	Jun-18	Dec-18	N/A	State	100%	100%	0.0%
ВС	SM	BC Pool Boiler Replacement SMSR 2017-18	28F767	2 - Construction	\$ 69,425	May-17	Dec-18	N/A	State	100%	99%	0.0%
CC	CAP	CC Main Building Modernization	FB1062	2 - Construction	\$ 20,558,037	Sep-15	Dec-18	Dec-18	SRID/Meaure J	100%	95%	16.0%
CC	SM	Mammoth Center Modernization	FB5023	2 - Construction	\$ 2,914,825	Jun-17	Jan-18	May-18	Mammoth	100%	95%	0.0%
CC	SM	CC Prop 39 Year 5	48F755	2 - Construction	\$ 116,477	Mar-18	Jul-18	N/A	Prop 39	100%	100%	0.0%
CC	SM	CC SMSR 2017-18 CDC Renovation	48F753	2 - Construction	\$ 131,462	Apr-18	Jul-18	N/A	State/Campus	100%	50%	0.0%
DO	CAP	District Wide Security Access Hardware	FD1025	2 - Construction	\$ 4,854,342	Apr-15	Apr-17	N/A	SRID	100%	99%	0%
DO	CAP	Network Systems	FD1020	2 - Construction	\$ 462,218	Jun-12	Ongoing	N/A	SRID	100%	90%	0.0%
DO	SM	Weill SMSR 20106-17 Weill Renovations	28F802	2 - Construction	\$ 118,695	Apr-18	Sep-18	N/A	State	100%	50%	
DO	SM	Weill Exterior Building Painting SMSR 2017-18	28F768	2 - Construction	\$ 128,250	Jun-18	Dec-18	N/A	State	100%	100%	0.0%
PC	SM	PC Prop 39 Year 5 Interior/Exterior Lighting	58F746	2 - Construction	\$ 126,956	Mar-18	Jun-18	N/A	Prop 39/Campus	100%	100%	0.0%
PC	SM	PC Replace FFE, Various Campus Locations	58F739	2 - Construction	\$ 229,870	Nov-17	Sep-18	N/A	SRID	100%	100%	0.0%
PC	SM	PC 2017-18 SMSR Door Hardware Replacement	58F744	2 - Construction	\$ 41,620	Apr-18	Oct-18	N/A	State/Campus	100%	95%	0.0%
PC	SM	PC SMSR 2016-17 High Voltage Electrical Improvemen	FC1090	2 - Construction	\$ 167,944	Nov-16	Nov-18	N/A	State/SRID	100%	100%	0.0%
PC	SM	PC Replace/Repair HVAC, Various Building	58F740	2 - Construction	\$ 26,494	Jul-17	Jan-19	N/A	SRID	100%	99%	0.0%
PC	SM	PC Campus Security Upgrades Phases 1 - 3	FC1010	2 - Construction	\$ 694,112	Aug-16	May-19	N/A	SRID/Campus	100%	99%	4.0%
PC	SM	PC Math/Science Elevator Repair	FC1083	2 - Construction	\$ 579,390	Jul-16	Jul-19	Nov-19	SRID	100%	95%	0.0%
PC	SM	PC 2017-18 SMSR HVAC Replacement	58F743	2 - Construction	\$ 64,230	Aug-18	Oct-18	N/A	State/Campus	100%	100%	0.0%
PC	SM	PC Gym Floor Replacement	58F753	2 - Construction	\$ -	Jul-19	Oct-19	N/A	Measure J	0%	0%	0.0%



District Program Overview Design Projects 1st Quarter September 30, 2018

Campus	Туре	Project Name	Project Organization Code	tal Project penditures	Start Date	Completion Date	Anticipated DSA Close Date	Project Funding Source	Construction /Design % Complete	Project % Complete	_
ВС	CAP	BC Veterans Resource Center	28F760	\$ 674,773	Apr-17	Nov-18	Nov-18	Measure J	100%	0%	0.0%
BC	CAP	BC Wireless Infrastructure	28F766	\$ 304,589	Sep-19	Jan-20	N/A	Measure J	40%	40%	0.0%
ВС	CAP	BC Campus Student Center (ABC)	28F763	\$ 1,948,857	Dec-18	May-20	Jun-20	SRID/Meaure J	100%	0%	0.0%
ВС	CAP	BC Infrastructure	28F792	\$ 3,321	Sep-19	Jun-20	Jun-20	Measure J	0%	0%	0.0%
ВС	CAP	BC Science & Engineering	28F796	\$ -	Dec-19	Jan-22	Jan-22	Measure J	0%	0%	0.0%
ВС	CAP	BC Combined Gym and Fieldhouse	28F790	\$ -	Feb-20	Sep-22	Sep-22	Measure J	0%	0%	0.0%
ВС	CAP	BC Facilities Master Plan	28F765	\$ 287,990		Dec-18	N/A	Measure J	90%	90%	0.0%
ВС	CAP	BC Arvin Education Center	28F762	\$ 71,204	Jan-20	Sep-24	Sep-24	Measure J	0%	0%	0.0%
BC	CAP	BC Swing Space Measure J	28F798	\$ 67,236	Jun-18	Dec-24	Dec-24	Measure J	0%	0%	0.0%
BC	SM	BC Memorial Stadium Phase 1	28F764	\$ 485,149	Oct-17	Oct-21	Oct-21	Measure J	25%	0%	0.0%
CC	CAP	CC East Kern Development	48F757	\$ -	Jan-19	Jul-20	7/720	Measure J	0%	0%	0.0%
CC	CAP	CC Physcial Education Outdoor Complex Renovation	48F758	\$ -	Jan-19	Jul-22	Jul-22	Measure J	0%	0%	0.0%
CC	Р	CC Facilities Master Plan	48F751	\$ 59,085	Apr-18	Dec-18	N/A	Measure J	99%	90%	0.0%
CC	SM	CC IWV Solar Upgrade Inverters	48F754	\$ -	Oct-18	Feb-19	N/A	Measure J	10%	1%	0.0%
CC	SM	CC Kern River Valley Modernization	48F752	\$ -	Oct-19	Jul-20	N/A	Measure J	10%	1%	0.0%
CC	SM	CC Art HVAC	48F759	\$ -	Jan-19	Dec-20	Dec-20	Measure J	0%	0%	0.0%
CC	SM	CC Monument/Digital Sign	48F760	\$ -	Jan-19	Sep-20	Sep-20	Campus	0%	0%	0.0%
CC	SM	CC Gym Floor Upgrade	48F750	\$ 49,625	Jul-18	Sep-18	N/A	Measure J	100%	75%	0.0%
DO	CAP	DO Public Address Notification	FD1026	\$ 41,341	May-17	Aug-17	N/A	SRID	80%	25%	0.0%
DO	CAP	DO/BC Public Address Systems Project	18F743	\$ -	Feb-18	Oct-18	N/A	SRID	0%	0%	0.0%
DO	CAP	DO/PC Public Address System Project	18F744	\$ -	Feb-18	Dec-18	N/A	SRID	0%	0%	0.0%
PC	CAP	PC Land Acquistion	58F748	\$ 3,000	Apr-18	Jun-20	N/A	Measure J	0%	0%	0.0%
PC	Р	PC Facilities Master Plan	58F741	\$ 197,839	Dec-17	Aug-18	N/A	Measure J	100%	95%	0.0%
PC	CAP	PC Infrastructure	58F752	\$ -	Mar-20	Oct-21	Oct-21	Measure J	0%	0%	0.0%
PC	CAP	PC Restroom Renovation & Hazard Material Removal	58F751	\$ 2,250	Mar-20	Oct-21	Oct-21	Measure J	0%	0%	0.0%
PC	SM	Parking Lot "A" & "B" Rehabilitaion	58F737	\$ 1,279,491	Apr-18	Oct-18		Campus	100%	99%	0.0%
PC	SM	PC Tennis Court Resurfacing	58F749	\$ -	Jul-18	Aug-18	N/A	SRID	100%	100%	0.0%
PC	SM	PC Drought Resistant Landscape	58F750	\$ -	Jun-18	Nov-18	N/A	Measure J	100%	65%	0.0%



District Final Project Proposal (FPP) and Initial Project Proposal (IPP) Planning Activities

Project	Total Budget	State Contribution	Local Contribution	Туре
Delano LRC Multi-Purpose Building	\$32,126,000	\$16,868,000	\$15,258,000	FPP
PC Allied Health Facility	\$21,578,000	\$10,967,000	\$10,611,000	FPP
FPP Total	\$53,704,000	\$27,653,000	25,869,000	
PC Career Technology Building	\$17,659,000	\$9,659,000	\$8,000,000	IPP
IPP Total	\$17,659,000	\$9,659,000	\$8,000,000	



BC Veterans Resource Center





BAKERSFIELD COLLEGE VETERANS RESOURCE CENTER





CC Main Building Modernization





PC Flooring Replacement, Various Buildings



PC Math Science Elevator Repairs



BOND OVERSIGHT COMMITTEE LISTING

Committee Chair- Jesse Frederick (March 2018-February 2020)

Vice Chair- Bruce Massa (October 2017-September 2019)

Matthew Anderson (December 2016-November 2018)

Doug Starr (February 2017-January 2019)

Rob Goff (February 2017-January 2019)

Steve Murray (February 2017-January 2019)

Cheryl M. Scott (February 2017-January 2019)

Paula De La Riva-Barrera (March 2017-February 2019)

Gregory D. King (March 2017-February 2019)

Richard Osborne (May 2017-April 2019)

Student Trustee:

Chrisman Sawyer (July 2018 – June 2019)



Questions?
