

DV BIEN'S

Facilities Planning & Construction Report 2021 – 22 November 3, 2021



BAKERSFIELD COLLEGE 1913-2013





Overview

- District Measure G Spending (MG100)
- District Measure J Spending (MJ100)
- District Program Overview
 - Completed Projects
 - Projects Under Design and Construction
 - State Funding Opportunities




District SRID Measure G Spending Summary (As of 10/26/2021)

- Original Measure G:
- Interest & Other Revenues:
- Total SRID Funds:
- Total Funds Spent To Date:
- Total Funds Encumbered:
- Total Funds Unspent To Date: \$

\$ 180,000,000
\$ 26,191,104
\$ 206,191,104
\$ 197,879,588
\$ 1,299,886
\$ 7,011,629



Measure G Allocations by College

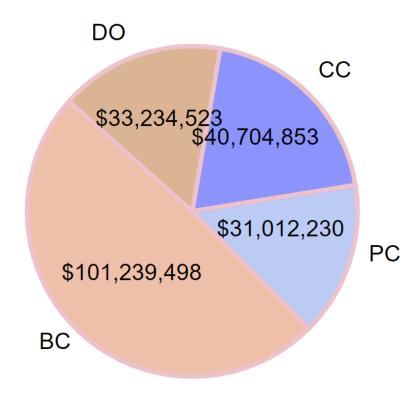


Total: \$206,191,104



Measure G Spent by College

(As of 10/26/2021)




Total: \$197,879,588



Measure G Encumbered by College

(As of 10/26/2021)



Total: \$1,299,886

District Measure J Spending Summary


(As of 10/26/2021)

Original Measure J Budget: \$ 502,820,956
Interest & Other Revenues: \$ 3,796,488
Total Measure J Funds: \$ 506,617,444
Total Funds Spent To Date: \$ 159,916,294
Total Funds Encumbered: \$ 86,343,121
Total Funds Unspent To Date: \$ 260,052,436





Measure J Allocations by College

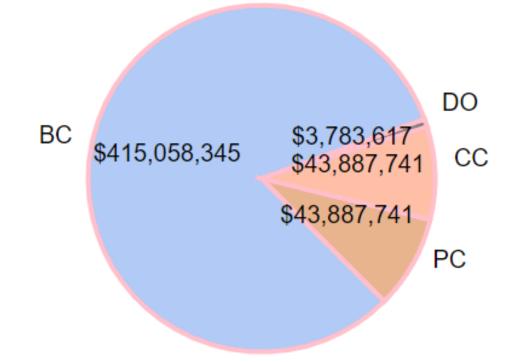


Total: \$506,617,444



Measure J Spent Funds by College

(As of 10/26/2021)




Total: \$159,916,293.59

*Does not include \$222,309 for Bond Payment and \$6,290,591.33 for Measure J Debt Service



Measure J Encumbered Funds by College

(As of 10/26/2021)



Total: \$86,343,120.82

Completed District Program Projects

Bakerstield College – Campus Center



District Program Overview

Completed Projects Report

Please enter date range for report. The default is one year ago from today. Start Date: October 26, 2020 End Date: October 26, 2021 Go This report is formated for landscape printing. Please remember to set your printer to landscape.

	Kern Community College District Facilities and Construction Group										
Completed Projects Report Date Range: October 26, 2020 to October 26, 2021											
Campus	Project Name	Project Organizational Code	Total Project Expenditures	Project Start Date	Project End Date	Funding Source(s)					
PC	ADA Doors	58F760	\$36,824	Oct 2019	Jan 2021	Other					
СС	Bishop Parking Lot Rehabilitation	48F762	\$675,084	May 2020	Nov 2020	Other					
PC	Campus Security Upgrades	FC1010	\$1,092,472	Jan 2017	Aug 2021	Meas. G Other					
BC	Campus Signage	28F785	\$229,421	May 2019	Apr 2021	Meas. J					
DO	First Floor Windows for Efficiency	18F754	\$69,730	Dec 2020	Apr 2021	Meas. G					
DO	Floorcovering Replacement (SMSR 2019-20)	18F749	\$25,000	Jun 2020	May 2021	SMSR					
BC	Humanities Phase 1 Elevator	28F815	\$133,796	Feb 2021	Jul 2021	Meas. J					
СС	IWV Solar Panel Upgrades - Inverters	48F754	\$829,413	May 2020	Jun 2021	Meas. J					
СС	Kern River Valley Modernization	48F752	\$32,960	Jan 2020	Dec 2020	Meas. J					
BC	Lighting Retrofit (SMSR 2019-2020)	28F813	\$127,095	Aug 2020	May 2021	SMSR Other					
сс	Main Building Modernization	FB1062	\$24,885,264	Sep 2015	Aug 2021	Meas. G Meas. J					
BC	Memorial Stadium	28F764	\$14,510,064	Feb 2020	Mar 2021	Meas. J					



District Final Project Proposal (FPP) and Initial Project Proposal (IPP) Planning Activities

Project	Туре	Total Budget	State Contribution	Local Contribution	Local Fund Source
BC Fine Arts Renovation/Replacement	IPP	\$15,548,483	\$11,744,807	\$3,803,676	Unknown at this time
IPP Total		\$15,548,483	\$11,744,807	\$3,803,676	
BC Center for Student Success	FPP	\$33,745,426	\$16,644,758	\$17,100,668	Unknown at this time
PC Career Technology Building	FPP	\$29,531,342	\$14,582,489	\$14,943,853	Measure J
FPP Total		\$63,276,768	\$31,227,247	\$32,044,521	
Grand Total		\$78,825,251	\$42,972,054	\$35,848,197	













Renegade Athletic Complex - Construction Complete April 2023

continued



Science & Engineering Building – Complete January 2022

continued





Administrative Services Building - Construction Complete May 2022

continued



Welcome Center - Construction Complete November 2023

continued



Delano Campus – LRC Multi-Purpose Building

Bids Construction Complete November 18, 2021 January 2022 Fall 2023




Arvin Educational Center

DSA ApprovalDecember 2021BidsSpring 2022CompleteJuly 2024



Ag Replacement Center

DSA Submittal	February 2022
Bids	Spring 2023
Complete	Winter 2024-25

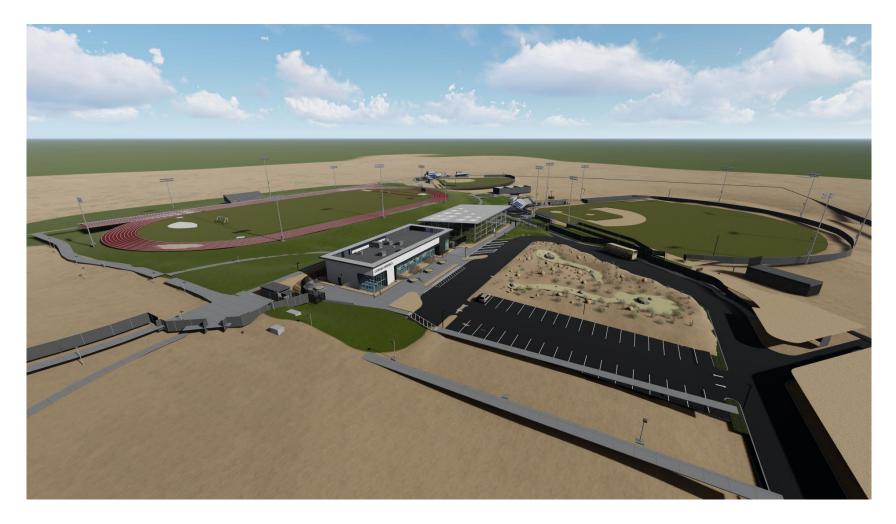

P.E. Outdoor Complex – DSA Approval in Dec. 2021 Project Complete - July 2024

continued





Upgrades to Baseball and Softball Facilities, and Track Replacement

continued





Main Building Lecture Hall Renovations

continued



New M & O Facility - Under Construction

Complete – January 2022


continued



Gymnasium Lighting and Building Upgrades



continued

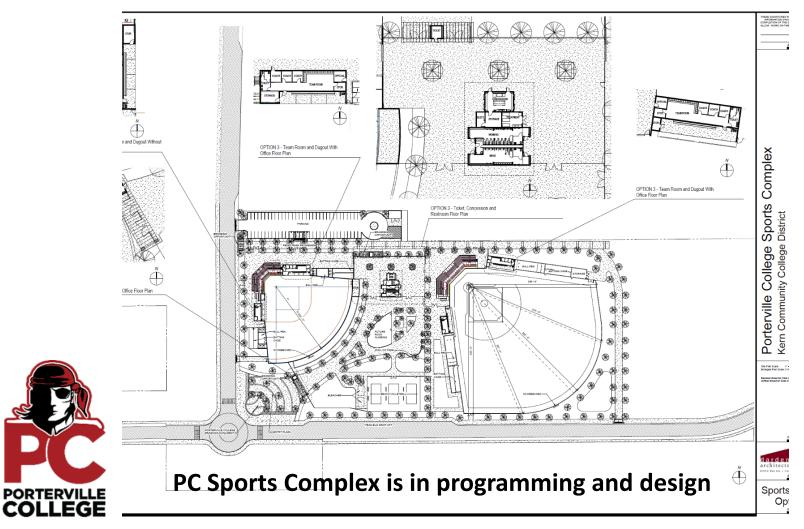



continued



Allied Health Building – Bids Nov. 9, 2021 - Est. Project Completion – July 2023

continued

Perspective Sketch - Future Career Technology (CTE) Building



Bond Oversight Committee Listing

Committee Chair- Paula De La Riva-Barrera (February 2021-January 2023)

Vice Chair- Matthew Anderson (February 2021-January 2023)

Rob Goff (February 2021-January 2023)

Steve Murray (February 2021-January 2023)

Jesse Frederick (March 2020-February 2022)

Gregory D. King (February 2021-January 2023)

Diane Foucher (December 2019-November 2021)

<u>Student Trustee</u> – Gian Gayatao (June 2021-June 2022)



