

3333

Facilities Planning & Construction Report 2021 – 22

March 31, 2022

572G *)



BAKERSFIELD COLLEGE 1913-2013





Overview

- District Measure G Spending (MG100)
- District Measure J Spending (MJ100)
- District Program Overview
 - Completed Projects
 - Projects Under Design and Construction
 - State Funding Opportunities




District SRID Measure G Spending Summary

(As of 03/22/2022)

Original Measure G: \$180,000,000
Interest & Other Revenues: \$26,044,461
Total SRID Funds: \$206,044,461
Total Funds Spent To Date: \$198,195,234
Total Funds Encumbered: \$2,749,638
Total Funds Unspent To Date: \$5,099,589



Measure G Allocations by College

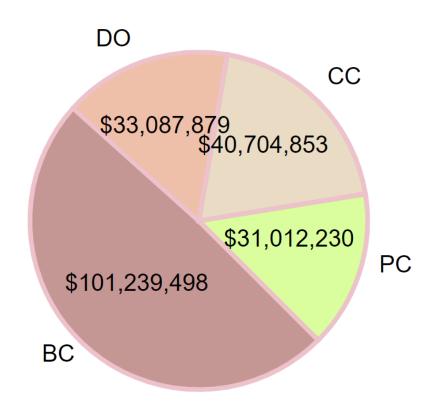


Total: \$206,044,460



Measure G Spent by College

(As of 03/22/2022)




Total: \$198,195,234



Measure G Encumbered by College

(As of 03/22/2022)



Total: \$2,749,638

District Measure J Spending Summary

\$502,820,956

\$508,783,084

\$ 190,993,501

\$ 75,364,607

\$


5,962,169

- Original Measure J Budget:
- Interest & Other Revenues:
- Total Measure J Funds:
- Total Funds Spent To Date:
- Total Funds Encumbered:
- Total Funds Unspent To Date: \$ 242,424,976





Measure J Allocations by College

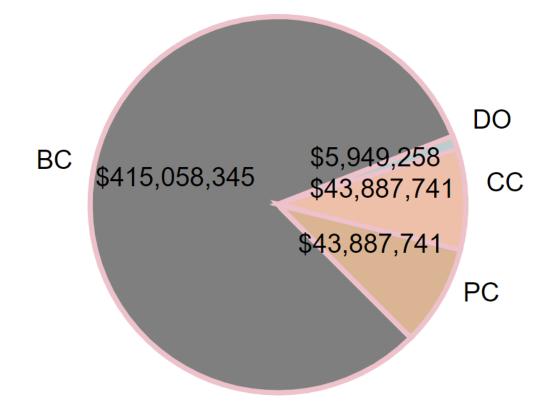


Total: \$506,617,444



Measure J Spent Funds by College

(As of 03/22/2022)




Total: \$190,993,501.14

*Does not include \$222,309 for Bond Payment and \$6,290,591.33 for Measure J Debt Service



Measure J Encumbered Funds by College

(As of 03/22/2022)



Total: \$75,364,607.13

Completed District Program Projects

Car

Bakersfield College – Campus Center



District Program Overview

Please enter date range for report. The default is one year ago from today. Go

Start Date:	March 22, 2021	End D)ate: March 22,	2

2022

 Start Date:
 March 22, 2021
 End Date:
 March 22, 2022
 Go

 This report is formated for landscape printing.
 Please remember to set your printer to landscape.

Kern Community College District Facilities and Construction Group						
Completed Projects Report Date Range: March 22, 2021 to March 22, 2022						
Campus	Project Name	Project Organizational Code	Total Project Expenditures	Project Start Date	Project End Date	Funding Source(s)
DO	ADA Path of Travel Upgrades SMSR 2021-22	28F823	\$75,000	Jan 2022	Mar 2022	SMSR
PC	Campus Security Upgrades	FC1010	\$1,092,472	Jan 2017	Aug 2021	Meas. G Other
BC	Campus Signage	28F785	\$229,421	May 2019	Apr 2021	Meas. J
DO	First Floor Windows for Efficiency	18F754	\$69,730	Dec 2020	Apr 2021	Meas. G
DO	Floorcovering Replacement (SMSR 2019-20)	18F749	\$25,000	Jun 2020	May 2021	SMSR
BC	Flooring Abatement and Replacement (SMSR 2019-2020)	28F811	\$47,231	May 2020	Nov 2021	SMSR
BC	Humanities Phase 1 Elevator	28F815	\$133,796	Feb 2021	Jul 2021	Meas. J
СС	IWV Solar Panel Upgrades - Inverters	48F754	\$829,413	May 2020	Jun 2021	Meas. J
PC	Kitchen Plumbing	58F755	\$284,061	Apr 2021	Nov 2021	Meas. J
BC	Lighting Retrofit (SMSR 2019-2020)	28F813	\$127,095	Aug 2020	May 2021	SMSR Other
сс	Main Building Modernization	FB1062	\$24,885,264	Sep 2015	Aug 2021	Meas. G Meas. J
BC	Memorial Stadium	28F764	\$14,510,064	Feb 2020	Mar 2021	Meas. J
BC	Memorial Stadium Maintenance Project	28F816	\$1,359,883	Dec 2020	Nov 2021	Meas. J
PC	Replace/Repair HVAC, Various Buildings	58F740	\$237,144	Jul 2017	Nov 2021	Meas. G
BC	Wireless Infrastructure	28F766	\$1,014,198	Aug 2018	Nov 2021	Meas. J

Measure G and J Projects Completed since 2018	34
Projects Under Construction	21
Projects in Design	11



(E) LOT P9

District Final Project Proposal (FPP) and Initial Project Proposal

(E) LOT P11

DSA APP#: 03-104296

(IPP)	Planning	Activiti	es renching for (N) Lectrical connection
-------	----------	----------	--

(E)

(E) LANGUAGE ARTS

HALL DSA APP#: 03-113971

> (E) FORUM DSA APP#: 27967

(E) GYMNASIUM DEP, PUBLIC WORKS A#: 03-115216

(E) ALLIED HEALTH

(E) MA SCI A#: 1

			2001	APPENDING OF THE	
Project	Туре	Total Budget	State Contribution	Local Contribution	Local Fund Source
BC Fine Arts Renovation/Replacement	IPP	\$15,548,483	\$11,744,807	\$3,803,676	Unknown at this time
IPP Total		\$15,548,483	\$11,744,807	\$3,803,676	
BC Center for Student Success	FPP	\$33,745,426	\$16,644,758	\$17,100,668	Unknown at this time
PC Career Technology Building	FPP	\$29,531,342	\$14,582,489	\$14,943,853	Measure J
FPP Total		\$63,276,768	\$31,227,247	\$32,044,521	
Grand Total		\$78,825,251	\$42,972,054	\$35,848,197	





Renegade Athletic Complex - Construction Complete April 2023

continued



Science & Engineering Building – Complete May 2022


continued





Administrative Services Building - Construction Complete May 2022

continued

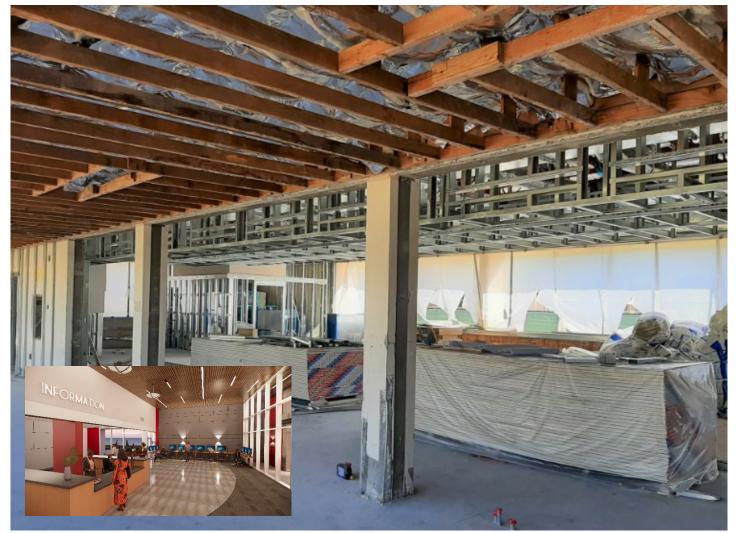

Welcome Center - Construction Complete November 2023

continued



Delano Campus Learning Resources Center - Complete July 2023

continued




Arvin Educational Center

DSA Approval	March 2022
Bids	Spring 2022
Complete	July 2024

Ag Replacement Center

DSA Submittal	March 2022
Bids	Spring 2023
Complete	Winter 2024-25



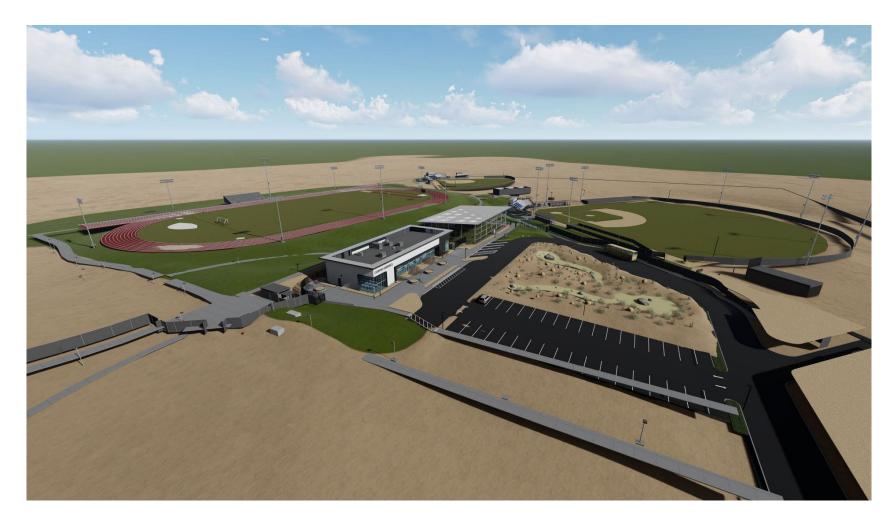


P.E. Outdoor Complex – DSA Approval in April 2022 Project Complete - July 2024

continued




continued

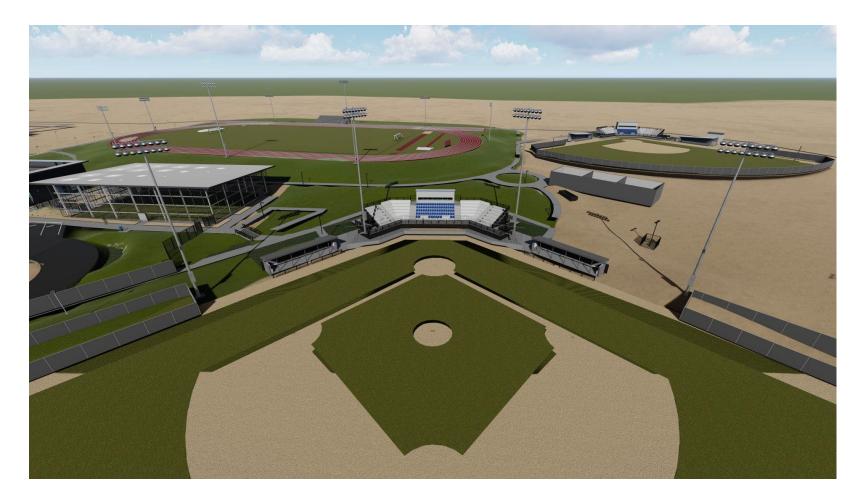

Upgrades to Baseball and Softball Facilities, and Track Replacement

continued

Gymnasium Equipment and Flooring Upgrades

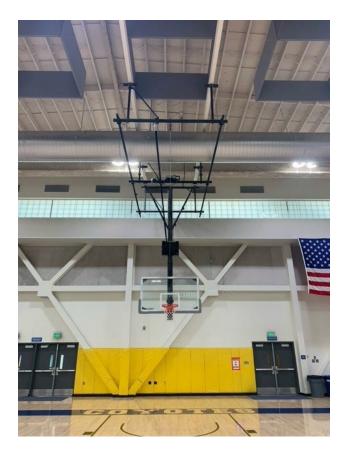



continued




New M & O Facility - Complete – January 2022

continued



New M & O Facility - Complete – January 2022

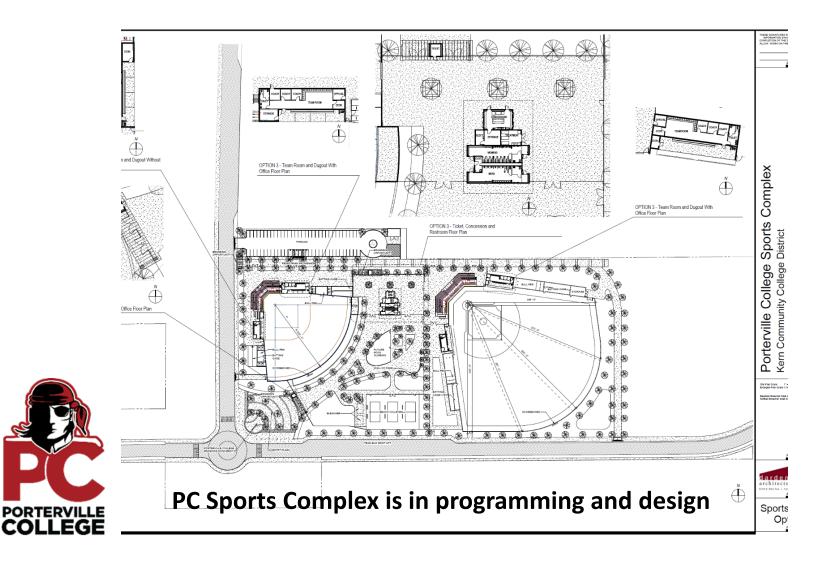

continued

PC Stadium Upgrade Project







continued



Allied Health Building – Under Construction Project Completion – January 2024 $_{28}$

continued

Perspective Sketch - Future Career Technology (CTE) Building



Bond Oversight Committee Listing

<u>Committee Chair</u>- Paula De La Riva-Barrera (February 2021-January 2023)

Vice Chair- Matthew Anderson (February 2021-January 2023)

Rob Goff (February 2021-January 2023)


Steve Murray (February 2021-January 2023)

Jesse Frederick (February 2022-January 2024)

Gregory D. King (February 2021-January 2023)

Diane Foucher (February 2022-January 2024)

<u>Student Trustee</u> – Gian Gayatao (June 2021-June 2022)



S

AINING AND GYMNASIUM

Μ

ŝ

SHOWER ROOM

CCESS AREA

ROOM

ON AREA

OM



FIELD LEVEL





