

Facilities Planning & Construction Report 2022 - 23

May 25, 2023



BAKERSFIELD COLLEGE 1913-2013





District Program Update

- District Measure G Spending (MG100)
- District Measure J Spending (MJ100)
- Program Activity Update
 - Completed Projects
 - State Funding Opportunities
 - Highlighted Campus Projects




District SRID Measure G Spending Summary

(As of 05/23/23)

- Original Measure G: \$180,000,000
- Interest & Other Revenues: \$ 26,117,593
- Total SRID Funds: \$206,117,593
- Total Funds Spent To Date: \$204,091,565
- Total Funds Unspent To Date: \$ 2,026,028



Measure G Allocations by College

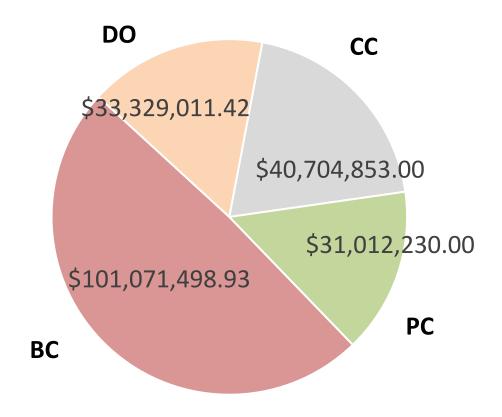

Total: \$206,117,593



Measure G Spent by College

(As of 05/22/23)



Total: \$204,091,565

District Measure J Spending Summary


(As of 05/24/2023

- Original Measure J Budget: \$502,820,956
- Interest & Other Revenues: \$ 5,962,169
- Total Measure J Funds: \$508,783,084
- Total Funds Spent To Date: \$250,866,771
- Total Funds Encumbered: \$ 75,358,676
- Total Funds Unspent To Date: \$ 182,557,637





Measure J Allocations by College

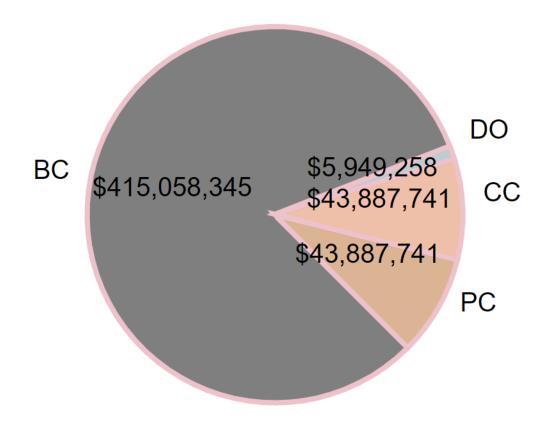


Total \$508,783,084



Measure J Spent Funds by College

(As of 05/24/2023)




Total: \$250,866,771



Measure J Funds Encumbered by College

(As of 05/24/2023)



Encumbered Total: \$75,358,675.22

Total Measure J Remaining Funds \$182,557,637.62





Recently Completed Projects

Kern Community College District Facilities and Construction Group

Completed Projects Report Date Range: January 01, 2022 to May 22, 2023

Campus	Project Name	Project Organizational Code	Total Project Expenditures	Project Start Date	Project End Date	Funding Source(s)
DO	ADA Path of Travel Upgrades SMSR 2021-22	28F823	\$75,000	Jan 2022	Mar 2022	SMSR
ВС	Ag Farm Road Improvements		\$0	May 2022	Apr 2023	Other
ВС	Campuswide Asbestos Floor Removal & Replacement, SMSR 2018-19	28F804	\$110,528	Dec 2019	May 2022	SMSR Other
ВС	Concrete Replacement Campuswide SMSR 2021-22	28F830	\$435,129	May 2022	Mar 2023	SMSR
ВС	Dean & Adah Gay Sports Complex Monument Sign	28F822	\$70,967	Nov 2021	Mar 2023	Other
ВС	Delano Interior Lighting Retrofit SMSR 2021-22	28F836	\$98,368	Jun 2022	Aug 2022	SMSR
CC	East Kern Development	48F757	\$33,900	Feb 2020	Mar 2023	Meas. J
CC	ESCC Bishop Fire Tank Renovation/Upgrades SMSR 2021-22	48F769	\$29,886	Feb 2022	Aug 2022	SMSR
PC	Gym Floor Replacement	58F753	\$719,998	Apr 2019	May 2022	Meas. J
PC	HVAC Upgrades for Server Rooms (Phase 1) SMSR 2021-22	58F765	\$52,840	Feb 2022	Aug 2022	SMSR
PC	Infrastructure	58F752	\$614,713	Mar 2021	May 2022	Meas. J
ВС	Infrastructure - New Parking & Sports Field Handrail and Painting Upgrades	28F847	\$56,183	Nov 2022	Mar 2023	Meas. J
ВС	Infrastructure AG Farm Irrigation Monitoring Automation System		\$0	Feb 2022	Mar 2023	Other
ВС	Infrastructure AG Fencing Improvements	28F819	\$364,527	Aug 2021	Nov 2022	Meas. J



Recently Completed Projects

	FacilitySoft, Completed Projects Report Pag							
Kern Community College District Facilities and Construction Group								
Completed Projects Report Date Range: January 01, 2022 to May 22, 2023								
Campus	Project Name	Project Organizational Code	Total Project Expenditures	Project Start Date	Project End Date	Funding Source(s)		
ВС	Infrastructure Phase 1 - Parking Lot Rehabilitation	28F761	\$3,902,642	Mar 2018	Mar 2022	Meas. J		
ВС	Learning Garden	28F818	\$385,809	Jul 2021	Sep 2022	Other		
DO	Lighting Retrofit - First Floor SMSR 2021-22	28F826	\$149,834	Feb 2022	Apr 2022	SMSR		
DO	Lighting Retrofit - Second Floor SMSR 2021-22	28F824	\$121,988	Feb 2022	Apr 2022	SMSR		
CC	Lighting Retrofit West Wing Building SMSR 2021-22	48F774	\$64,218	Apr 2022	Nov 2022	SMSR		
CC	Lighting Upgrades Multiple Buildings SMSR 2021-22	48F775	\$44,994	Apr 2022	Jul 2022	SMSR		
CC	LRC Boiler Replacement SMSR 2021-22	48F776	\$68,749	Feb 2022	Aug 2022	SMSR		
CC	M&O Facility	48F765	\$2,094,169	Jun 2021	Sep 2022	Meas. J		
CC	Main Building Lecture Center Update	48F764	\$458,389	May 2020	Mar 2023	Meas. J		
CC	Main Building Roof Coating SMSR 2021-22	48F779	\$238,921	Mar 2022	Sep 2022	SMSR		
CC	Maintenance Building Renovation/Repairs SMSR 2021-22	48F778	\$34,771	Jan 2022	May 2022	SMSR		
CC	Occupational Lab Gate Replacement SMSR 2021-22	48F780	\$42,972	Feb 2022	Jun 2022	SMSR		
ВС	Rekey Campus SMSR 2021-22	28F828	\$19,160	Feb 2022	Apr 2023	SMSR		
ВС	Roof Replacement - Language Arts SMSR 2021-22	28F839	\$61,621	Aug 2022	Apr 2023	SMSR		
ВС	Simulation Lab	28F817	\$0	Dec 2021	Jan 2023	Other		

Measure G and J Projects Completed since 2018	50
Projects Under Construction	16
Projects in Design	11



(E) LANGUAGE ARTS

DSA APP#: 03-113971

(E) FORUM

District Final Project Proposal (FPP) and Initial Project Proposal (IPP) Planning Activities

DSA APP#: 03-104296

(E) LOT P9

SWIMMING POOL

DEP. PUBLIC WORKS DIV. ARCHITECTURE APP#: 11714 (06/11/1954)

Project	Туре	Total Budget	State Contribution	Local Contribution	Local Fund Source
PC Career Technology Building	FPP	\$36,767,543	\$18,526,101	\$18,241,442	Measure J
BC Fine Arts Replacement	FPP	\$38,120,846	\$28,628,847	\$9,491,999	Unknown at this time
FPP Total		\$74,888,389	\$47,154,948	\$27,733,441	
No IPPs Submitted					
IPP and FPP Grand Total		\$74,888,389	\$47,154,948	\$27,733,441	

AIN ENTRY

W HARDSCAPE

W LANDSCAPE


DESTRIAN PATH

HICULAR ROAD

DSA APP #03-118531



Science & Engineering Building – Construction Complete

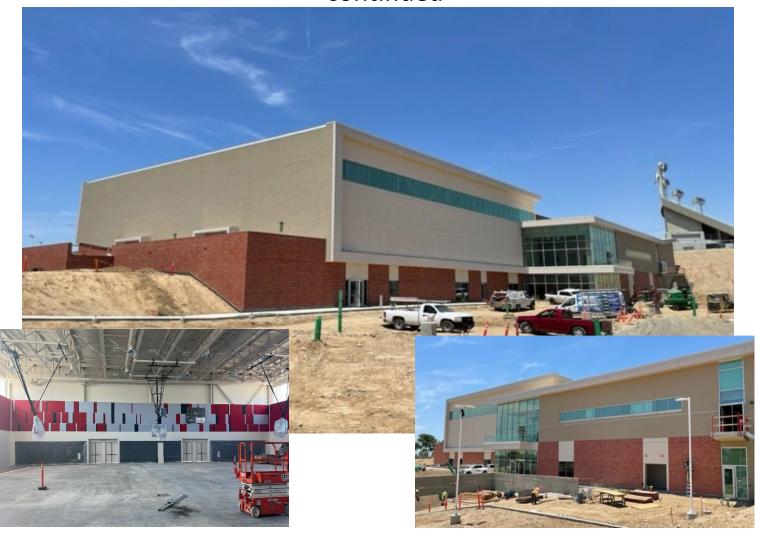

Renegade Athletic Complex - Construction Complete March 2024












Administrative Services Building - Construction Complete






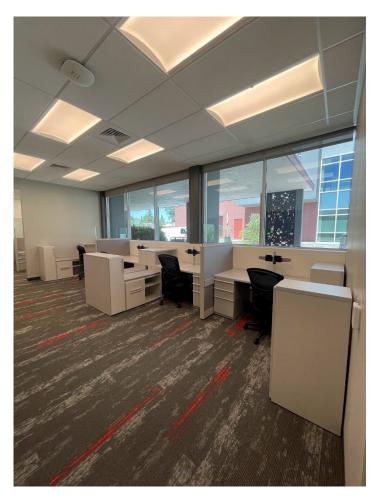





Administrative Services Building - Construction Complete









Delano Campus Learning Resources Center - Complete July 2023



Arvin Educational Center- Complete July 2024

continued



Agriculture Building Replacement

Bids
Construction Starts
Complete /Occupied

May 24, 2023 August 2023 November 2025





CERRO COSO COMMUNITY COLLEGE














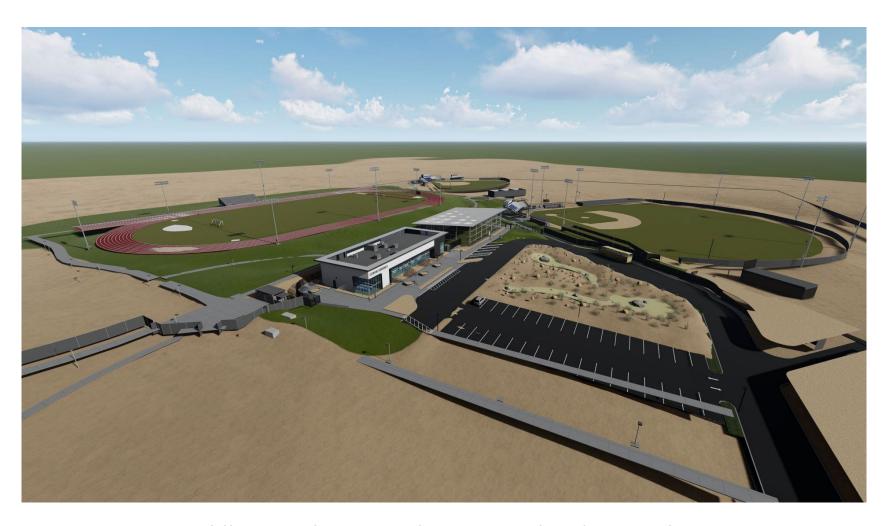

New Fieldhouse, Player Development and Parking Facilities
Upgrades to Baseball and Softball Facilities

continued

Gymnasium Renovation and Upgrades







continued

Gymnasium Renovation and Upgrades









Porterville College Project

PC Allied Health Building











Porterville College Projects


continued

PC Stadium Upgrade Project



Porterville College Projects


continued

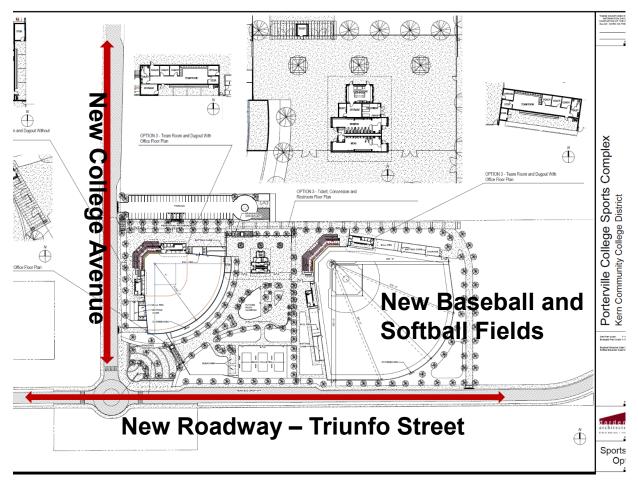



College Avenue Realignment – Fall 2023 PC Sports Complex – Awaiting Final DSA Approval

Porterville College Projects

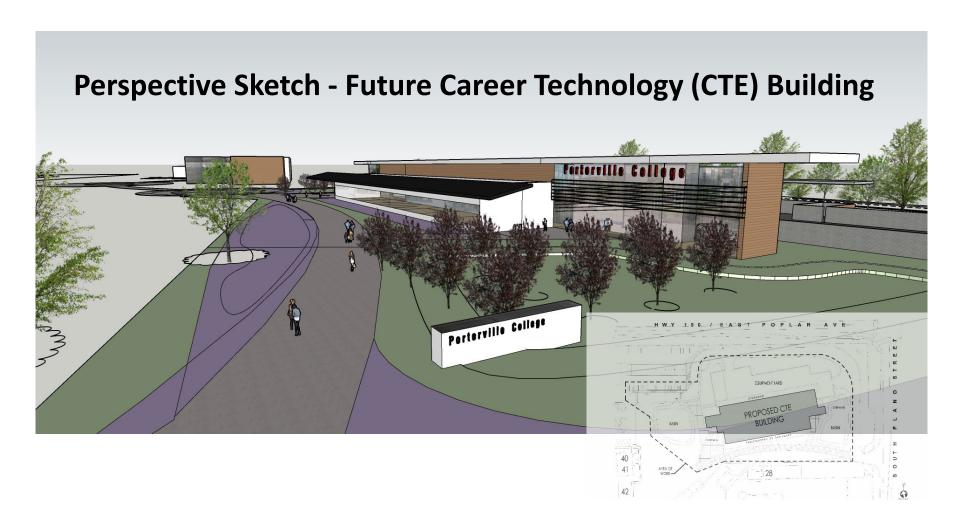

Bond Oversight Committee Listing

Jesse Frederick (February 2022 - January 2024)

Diane Foucher (February 2022 - January 2024)


Leigh Ann Cook (May 2023 - April 2025)

Richard Ellis (May 2023 - April 2025)

Martin Lonza (May 2023 – April 2025)

Paul Pavletich (May 2023 - April 2025)

Student Trustee - Shehrazad Barraj (June 2022 - June 2023)



AINING AND GYMNASIUM

SHOWER ROOM


CCESS AREA

ROOM

ON AREA

MO







BAKERSFIELD COLLEGE 1913-2013

